

Site Specific Safety Plan

Site Specific Safety Plan

The purpose of this document is to identify, document, and control hazards which are specific to this site to ensure that Duncan & Taylor Ltd is creating a safe working environment for all people who will be on site. It will include a register of the hazards that have been identified on this site and a list of the implement controls which aim to eliminate or minimise the risks associated with them. As part of Duncan & Taylors due diligence, subcontractors will have to provide SSSPs or a JSA or TA when applicable and it will be attached

1

General site information

Internal Ref:	J-13597	Date:	11/09/2023			
Project Name:	45 Mark Avenue, Paparangi Start Date: 25/09/2023					
Site Address:	45 Mark Avenue, Paparangi					
Project Manager:	Andrew Kelly	Contact:	027 647 0010			
Safety Manager:	Jonathon Bray	Contact:	022 437 4782			

2

Description of works

SCOPE

Garage - Downstairs

- · Supply and install new timber back door including glazing and hardware
- Decorate new door
- · Supply and install new cladding and decorate exterior wall to match existing. (Using BGC 9mm

Durascape board and batten to match as close as possible)

- · Supply and install new fence posts and chain link fence
- · Supply and install new 13mm Gib wall linings on all affected walls, stop and decorate walls
- · Supply and install skirtings and decorate
- · Remove and replace interior door leading into the gym/storage room and decorate
- · Seal and paint interior stairwell door and frame
- · Disconnect, store and refit hot points
- Rubbish removal

Hazards present on site

The below hazards have been identified and then a systematic approach to minimise risks associated has been implemented using the hierarchy of controls framework. For more information about the assessment tool please see the back page.

Hazard description	Caused by	Probibility	Severity	Risk rating	Controls	Probibilitiy	Severity	Risk rating
Activities that create risks to eyes, hands or heads	Overhanging items, items falling, airborne particulates, tool usage	Medium	Medium	Moderate	To ensure that appropriate PPE is being worn for the specific task being carried out i.e safety glasses when cutting wood with a saw. Prior To conducting any work which could create these risks workers in the area are informed so they can put on correct PPE or leave the area until it is safe To return	Low	Low	ACCEPTABLE
Activities or processes that could affect the public or other workers	Working in or open to the public, working in an area which other workers a present	Medium	Low	MODERATE	To have the worksite fenced off as much as reasobably practicable. To have appropriate room for vehicles to come into the workspace. To have a hazard board outside the site to alert the public to the works and instructing them not to enter. Inform all works prior to work begin where the exclusion zone is and not to enter	Medium	Very Low	ACCEPTABLE
Generation of noise in excess of 85db	PLANT, equipment, or processess	High	Medium	SEVERE	To wear level 5 ear protection when creating or being around any noise which could be above 85db. To make sure if anyone is going to create noise above 85db they inform the people working around so they can either leave the space, or put on level 5 ear protection	Medium	Low	MODERATE
Truck Loading and unloading	Strenuous activity related to unload or loading equipment or materials	Medium	Low	MODERATE	Make sure the vehicle has its handbrake on and has fully stopped. Keep the unloading/ loading area clean and free to trip hazards. Loading/ unloading area should be free to traffic. Ensure loads are secured correctly. Make sure workers are trained to be able lift objects correctly. Avoid lifting anything above 25kg without another person to help	Low	Low	ACCEPTABLE
Ladders	Needing to gain elevation for works	High	High	EXTREME	Eliminate the need to work from a ladder if possible. Assess if scaffold is a resonably practicable means to complete the works over the use of a ladder. Inspect ladder prior to use to ensure it is fit for purpose. Set up ladder on stable and level surface. Use the 4 to 1 rule where applicable. Ensure 3 points of contact at all times. Ensure that nothing above the thrid rung is used. Only use industrial garded ladders with rubber footings to prevent slipping. Always face the ladder while climbing it. Never try to reach further than	Low	Medium	Moderate
Use of powered saws	Using powered saws and other similar equipment recklessly or without attention	Medium	High	SEVERE	Ensure all equipment is inspected prior to use and is fit for purpose. Ensure all safe gaurds and other engineered controls and inplace prior to use. Use as manufacturer intended. Wear all required PPE when using.	Low	Low	ACCEPTABLE
Direct drive nail guns	Using direct drive nailguns and other similar equipment recklessly or without attention	Medium	Medium	Moderate	Ensure that the nail gun is inspected and is fit for use. Ensure that you have been trained to use such a device, and if not, then inform the foreman right away. Ensure that all in close proximity are aware that a direct dive nail gun is in use and not come closer while in use. Use as manufacturer intended.	Low	Low	ACCEPTABLE

_
4

Subcontractors

 \boxtimes Yes \square No Will subcontractors be used during this project? If yes then please name the below:

Adam Tulloch electrical	
Paintline decorators	
Fresh kitchens	
L B White	

□Yes ⊠No

Do any subcontractors need to provide an SSSP, JSA or Task analysis prior to works starting?

5

Particularly hazardous work and Worksafe notification

If any of the below works are being conducted, then a JSA or task analysis will be needed. These will be made by the people conducting the work and people who are sufficiently trained in the work to try encompass all risks that will result.

- Operation of PLANT, and heavy machinery
- Traffic management
 Anything requiring or
- Anything requiring an engineer
- Live electrical works
- Works over 1 story or (5m)
- Public works
- Asbestos works
- Hot works
- Confined spaces
- Blackwater
- Structural demolition
- Creation of openings which can be fallen through
- Any solvent-based paints or cleaners
- Mold
- Excavations
- Hazardous substance use

□Yes ⊠No

Does Worksafe need to be notified about any of the works being conducted?

6

Personal Protective Equipment to be worn on site





















Other

Please note - High Viability will be worn on all sites

If other please specify: Respirator when installing insulation

7

Onsite communication and review methods

What will be the regularity of the following while works are being conducted

Toolbox talks: Pre-start meetings: Before each stage

Site audits: Progress meetings: Fortnightly

Declaration

PCBU 1 (Duncan & Taylor Ltd)

		/	
Signed by:	Jonathon Bray	Date:	11/09/2023
Signature:	Lebour		
Before	e signing, please make sure you understand	d the belo	w statement.
	PCBU 2 (Contractor)		
Signed by:		Date:	
Signature:			
	DODIL 2 (Cub a antwa ata)	1	
Ciara ad bur	PCBU 3 (Subcontractor		
Signed by:		Date:	
Signature:			

By signing this document, you confirm that you have read and understand the information provided, and that you have conducted a risk assessment of the work site to the best of your ability for the works you have been engaged to conduct. You acknowledge the potential hazards associated with the works and understand your role as a Subcontractor on Duncan & Taylor Ltd's work site. You also understand your health and safety responsibilities and obligations as a subcontractor and to any employees under your supervision while on the site. You further acknowledge that any breaches of Duncan and Taylor Ltd's requirements and procedures may result in your immediate removal from the site and may lead to legal action being taken against you, where applicable. This statement is intended to remind you of the importance of providing accurate information and conducting a thorough risk assessment of the work site. It also emphasizes your responsibilities to follow Duncan and Taylor Ltd's health and safety requirements and procedures, and the consequences of failing to do so. By signing this document, you agree to comply with these requirements and procedures to the best of your ability and acknowledge the potential legal consequences of any breach.

Hazardous substance register

Name of substance	Location of SDS	Amount on site (volume)	UN Class (Section 14 SDS)	HSNO or GHS number (Section 14-15 SDS)	Classification	Location on site if stored	PPE requirements
Resene Turps	In yellow box with first aid kit	11	1300	GHSR002652	Solvent/ Flammable Toxic 6.7	In work vehicle	Gloves, respirator, body covering, covered footwear, glasses

Training register

Name	Role on site	First aid trained?	Relevant training	Years of experience
Andrew Kelly	☑ Project manager☑ Worker	⊠Yes □No	Project manager, registered builder, first aid level 1	15
Bruno Mello	□ Project manager⊠ Worker	□Yes ⊠No	First year apprentice	1
	□ Project manager□ Worker	□Yes □No		
	☐ Project manager ☐ Worker	□Yes □No		
	□ Project manager□ Worker	□Yes □No		
	□ Project manager□ Worker	□Yes □No		
	□ Project manager□ Worker	□Yes □No		

Hazard management system

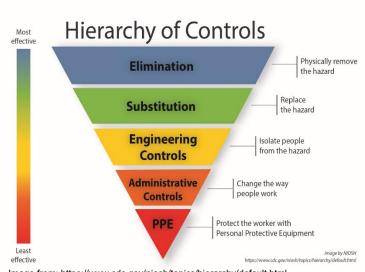


Image from: https://www.cdc.gov/niosh/topics/hierarchy/default.html

When a hazard is identified on site by employees and/ or subcontractors, the hierarchy of controls (see diagram to the left) is then used to discover solutions which either eliminate or minimise exposure to the risks associated with those hazards. In any context, elimination of a risk should be the first step if reasonably practicable. The Hierarchy of controls framework has five tiers in which elimination is the most effective strategy, then all others such as substitution and PPE are minimisation controls. This is used to evaluate the potential effectiveness of controls as how they will change the risk profile of the hazard.

Below is a risk matrix which is used to determine the potential risk of any such hazard of process. With probability on the X axis and Severity in the Y axis. The aim of any controls is to shift the probability and severity so that it becomes less hazardous for those conducting the works. The ability for controls to change the probability or severity will in turn shift the rating on the matrix to a more tolerable level.

Master Risk Matrix								
Se	Severity: Very Low Low Medium High Very High							
	Very High	MODERATE	SEVERE	SEVERE	EXTREME	EXTREME		
ity	High	ACCEPTABLE	MODERATE	SEVERE	EXTREME	EXTREME		
Probability	Medium	ACCEPTABLE	MODERATE	Moderate	SEVERE	EXTREME		
Pre	Low	ACCEPTABLE	ACCEPTABLE	Moderate	SEVERE	EXTREME		
Image from:	Very Low	ACCEPTABLE	ACCEPTABLE	ACCEPTABLE	MODERATE	SEVERE		

Severity key

Very High = If event occurs, likely more than one person will suffer severe illness, injury, or death **High** = If event occurs, one person will suffer from severe illness, injury, or death

Medium = If event occurs, one person will suffer from non-life threatening but severe illness or injury

Low = If event occurs, one person will suffer from mild illness or injury

Very low = If event occurs, one person will suffer from minimal illness or injury

SITE SPECIFIC RISKS BEFORE CONTROLS (PRE)								
Severity: Very Low Low Medium High						Very High		
	Very High							
ity	High			1	1			
Probability	Medium		2	2	1			
Ē	Low							
	Very Low							
	SITE SPECIFIC RISKS AFTER CONTROLS (POST)							
Sev	erity:	Very Low	Low	Medium	High	Very High		
	Very High							
ity	High							
Probability	Medium	1	1					
<u>C</u>	Low		4	1				

Very Low

Other Notes and comments applicable

mitigated though control Taylor will implement all	power tools and ladders comes with inherent risk which can never be fully ls, only minimised to a great extent. Because of this even though Duncan and controls they can to provide a safe working environment for people on our sites, sponsibility to ensure they are using the equipment as intended, and to only do uisite training for.

Emergency Response Plan						
Site address	45 Mark Avenue, Papa	arangi				
Supervisor name:	Andrew Kelly	Supervisor o	contact:	027 440 8593		
Emergency situation	IS					
⊠ Injury		☐ Gas leal	k			
☐ Earthquake		☐ Hazardo	ous substan	ce spill		
☐ Fire		☐ Floodin	g			
		⊠ Other –	propping fa	ilure		
F	Please describe the site	e specifics relat	ing to an eme	ergency		
		emergency help	if required.	eponse		
Site H&S manager:	Jonathon Bray		Contact:	022 437 4782		

Contact:

Contact:

027 647 0010

027 647 0010

Andrew Kelly

Andrew Kelly

First aider:

Site Foreman:

How will all be notified of an emergency: Air horn

First aid kit location: In the yellow box in the front door

Assembly point: On the conner of Mark Avenue and Tina Avenue

Worksafe contact: 0800 030 040

Nearest medical center location: 15 Batchelor Street, Newlands, Wellington 6037

Nearest medical center contact: 044789858

Hospital contact: 045666999

Civil Defense contact: 042375089

Poison Center contact: 0800 764 766

